




2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

Status Report # 1, April 12, 2019

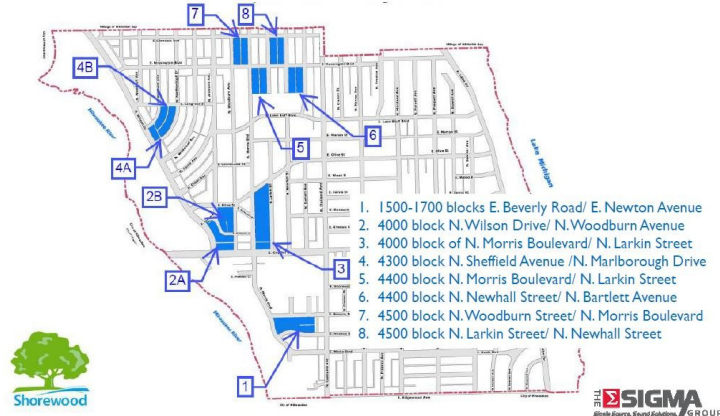

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

WORK COMPLETED FROM April 8, 2016 THROUGH April 12, 2016

Property owners adjacent to the alleys within the project limits were notified by letter and door notices of the scheduled work.

Construction activities began this week in alleys 5,6,7 and 8 with marking out the project limits and pavement sawing.

All-Ways Contractors began removal of the pavements in these alleys on Tuesday. It is anticipated that all alley pavement will be removed by the end of the week within alleys 5,6,7 and 8.

WORK SCHEDULED FOR THE WEEK OF April 15, 2016

Saw cutting of the alley pavements will continue this week and be completed in all alleys.

All-Ways Contractors will begin excavation of the subgrade in alleys 5,6,7 and 8. As the excavation is completed, aggregate base (gravel) will be placed and graded. At this time the Contractor will place temporary gravel ramps so access to garages will be restored until a point when asphalt pavement is placed.

Alley access will be unavailable until aggregate base is placed.

If you have any questions or special needs please feel free to contact one of the following:
Chris Ball, Onsite Representative - 262-388-0705
Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019 Alleys](http://www.villageofshorewood.org/2019%20Alleys)
