




2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

Status Report # 2, April 19, 2019

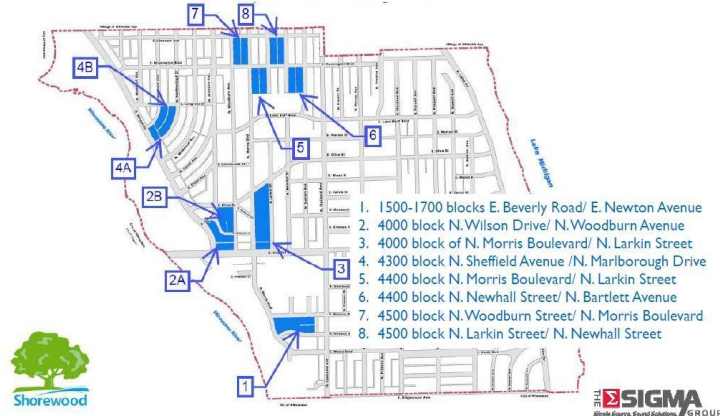

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

WORK COMPLETED FOR THE WEEK OF April 15, 2019

All Ways Contractors began excavation of subgrade in alleys 5, 6, 7 and 8. Pavement removal was completed in alley 7. After excavating the subgrade, an aggregate base (gravel) was placed and graded. It is anticipated that all the excavation and backfilling of base in alleys 5, 6, 7 and 8 will be completed by the end of the week.

With asphalt pavement tentatively scheduled to be placed the week of April 29th, Access to garages will remain restricted until the point when asphalt pavement is placed.

Property owners adjacent to alleys 4B and 2B were notified via letter and door notices of scheduled work.

WORK SCHEDULED FOR THE WEEK OF April 22, 2019

All Ways Contractors will begin fine grading in alleys 5, 6, 7 and 8 in preparation for asphalt pavement.

Pavement removal and excavation of subgrade in alleys 2B and 4B will begin Monday. Once removals and excavations are complete, aggregate base (gravel) will be placed and graded. ***Alley access will be unavailable until aggregate base is placed.***

If you have any questions or special needs, please feel free to contact one of the following:

Chris Ball, Onsite Representative - 262-388-0705

Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019 Alleys](http://www.villageofshorewood.org/2019%20Alleys)
