




# 2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

## Status Report # 3, April 26, 2019

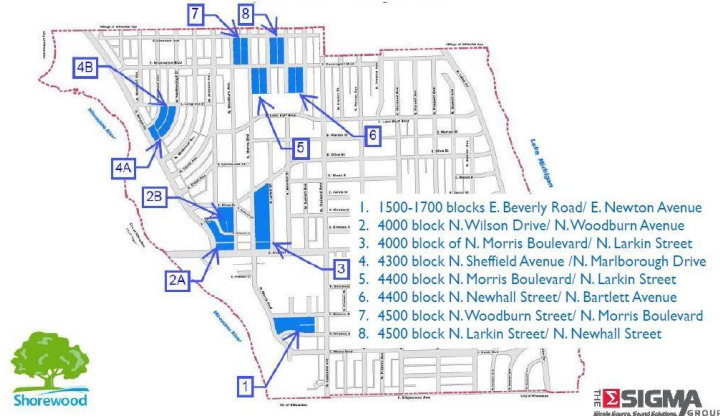

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

### **WORK COMPLETED FROM April 22, 2019 THROUGH April 26, 2019**

Pavement removals, subgrade excavation, and aggregate base placement were completed in alleys 4B, 2B and 3. All Ways Contractors completed finishing grades in preparation for asphalt paving in alleys 5, 6, 7, 8, 2B and 4B. Access to garages will remain restricted until the point when asphalt pavement is placed.

All Ways began pavement removal in alley 1.

Property owners adjacent to alleys 3 and 1 were notified via letter and door notices of scheduled work.

### **WORK SCHEDULED FOR THE WEEK OF April 29, 2019**

Stark Pavement will begin asphalt paving on Monday (weather dependent) in alleys 5, 6, 7, 8, and 2B.

Pavement removal and excavation of the subgrade will continue in Alleys 1, 2A, and 4A. Once pavement removal and excavation is completed, the Contractor will install the aggregate base (gravel) and begin preparing for paving.

***Alley access will be unavailable until paving operations are completed.***

If you have any questions or special needs please feel free to contact one of the following:

Chris Ball, Onsite Representative - 262-388-0705

Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019 Alleys](http://www.villageofshorewood.org/2019%20Alleys)
