




# 2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

## Status Report # 4, May 3, 2019

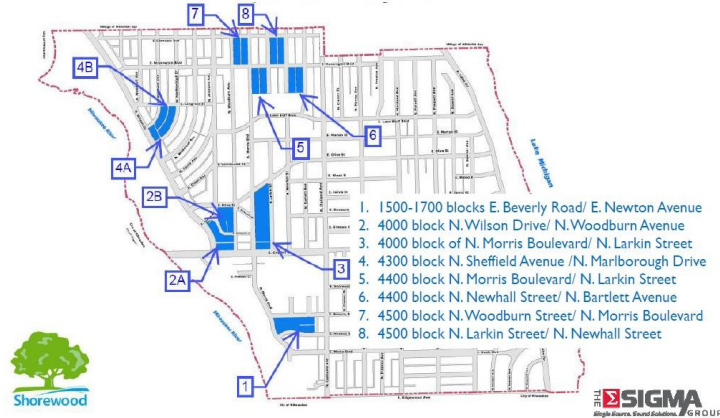

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

### **WORK COMPLETED FROM April 29, 2019 THROUGH May 3, 2019**

Pavement removals, subgrade excavation, and aggregate base placement were completed in alleys 1, 3 and 4A. All Ways Contractors completed finishing grades in preparation for asphalt paving in alleys 4B. Storm sewer pipe and a new catch basin was installed in alley 4A.

Due to weather related issues, asphalt paving did not take place this week as previously planned. Access to garages will remain restricted until the point when asphalt pavement is placed.

### **WORK SCHEDULED FOR THE WEEK OF May 6, 2019**

Stark Pavement will begin asphalt paving on Monday (weather dependent) in alleys 5, 6, 7, 8, 4B, and 2B. Base aggregate will be placed and fine graded in Alley 4A starting Monday. All Ways will begin pavement removal and excavation of subgrade in alleys 2A starting Tuesday. Once removals and excavations are complete, aggregate base (gravel) will be placed and graded.

### ***Alley access will be unavailable until paving operations are completed.***

If you have any questions or special needs please feel free to contact one of the following:

Chris Ball, Onsite Representative - 262-388-0705

Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019alleys](http://www.villageofshorewood.org/2019alleys)
