




# 2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

## Status Report # 5, May 10, 2019

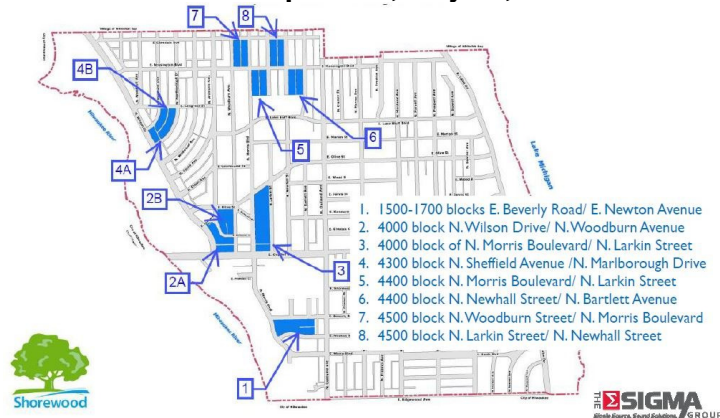

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

### **WORK COMPLETED FROM May 6, 2019 THROUGH May 10, 2019**

All Ways Contractors completed finish grading in preparation for concrete paving in alley 4A. Pavement removal and subgrade excavation took place in alley 2A followed by the installation of geotextile liner, storm sewer pipe and a new catch basin.

Stark Pavement completed the first layer of asphalt paving in alleys 1, 2B, 3, 4B, 5, 6, 7 and 8. Stark will return to complete the surface layer of asphalt once the all remaining work has been completed in these alleys.

### **WORK SCHEDULED FOR THE WEEK OF May 13, 2019**

TP Concrete will begin concrete paving of sidewalk and alleyway aprons on Monday (weather dependent) in alleys 1, 2B, 3, 4A, 4B, 5, 6, 7 and 8. Base aggregate will be placed and fine graded in Alley 2A starting Monday. Once fine grading is complete, concrete surface paving will commence in alley 2A and 4A.

*Alley access has been restored in the alleys with asphalt pavement in place. Residents are allowed to utilize the alley until final paving takes place in which notification will be made. Please use caution as construction work will still be taking place in various areas of these alleys. Alley access remains restricted in Alleys 4A and 2A while concrete pavement is being constructed.*

If you have any questions, please feel free to contact one of the following:

Chris Ball, Onsite Representative - 262-388-0705

Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019 Alleys](http://www.villageofshorewood.org/2019%20Alleys)
