




# 2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

## Status Report # 6, May 17, 2019

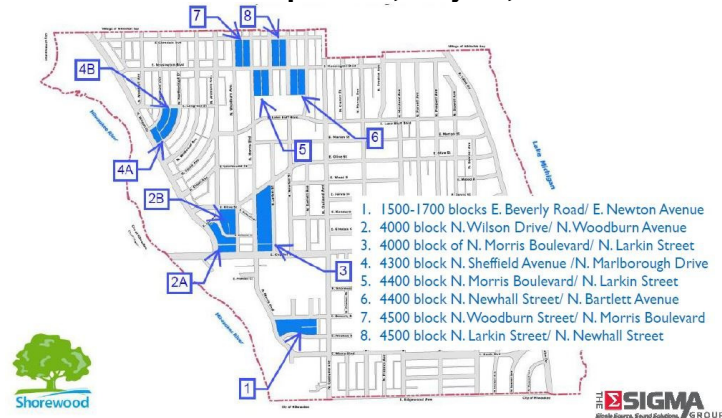

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

### **WORK COMPLETED THE WEEK OF MAY 13<sup>th</sup>, 2019**

All Ways Contractors completed finishing grades and other preparation work for concrete paving in alley 2A and the alleyway approaches at alley 2A, 4B, and 8.

T.P. Concrete poured the concrete in the west half of alley 4A and the north half of alley 2A. Concrete forming and pouring for the remainder of 4A and 2A is continuing as weather allows.

Access to garages in alleys 4A and 2A will continue to be restricted until concrete is cured and paver bricks are placed.

### **WORK SCHEDULED FOR THE WEEK OF May 20, 2019**

TP Concrete will continue concrete paving in alleys 4A and 2A. Removals and concrete paving of select approaches, sidewalks and alleyway entrance aprons will begin on Monday (weather dependent) in alleys 1, 2B, 3, 4A, 4B, 5, 6, 7 and 8.

***Alley and/or garage access will be unavailable in select Alleys until concrete paving operations are completed. Residents will be notified in advance of proposed alley closures via notice in front door.***

If you have any questions, please feel free to contact one of the following:

Chris Ball, Onsite Representative - 262-388-0705

Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019 Alleys](http://www.villageofshorewood.org/2019%20Alleys)
