




2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

Status Report # 8, May 31, 2019

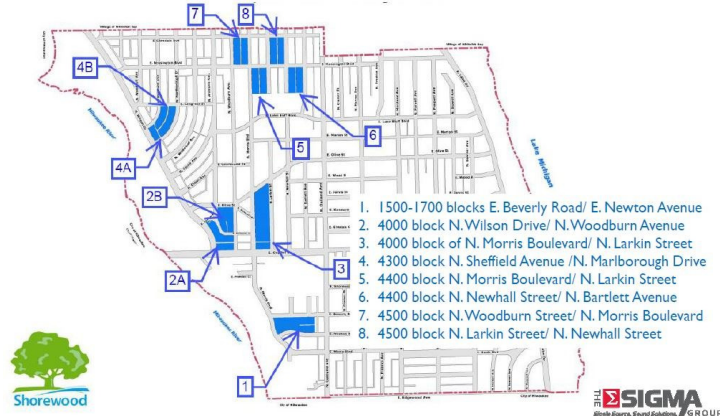

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

WORK COMPLETED For THE WEEK OF May 27th, 2019

All Ways Construction prepped alleys 2A and 4A for installation of brick pavers. Access to garages in alleys 4A and 2A will continue to be restricted until brick pavers are installed.

T.P. Concrete completed miscellaneous concrete repairs through the project site.

WORK SCHEDULED FOR THE WEEK OF June 3rd, 2019

Installation of the brick pavers in Alley 2A and 4A is scheduled for Wednesday June 5th. Breckenridge Construction has indicated this work is 2 to 3-day process and is anticipating being completed by the end of the week.

Stark Asphalt is scheduled to begin installation of the asphalt surface on Tuesday June 4th for alleys 1, 2B, 3, 4B, 5, 6, 7, and 8. This paving operation is anticipated to be completed in 1 to 2 days. Once the asphalt surface has been installed, alley access will be restored for use by adjoining property owners.

All – Ways Contractors will begin restoration of the disturbed grass areas once the asphalt pavement is completed.

If you have any questions please feel free to contact one of the following:

Chris Ball, Onsite Representative - 262-388-0705

Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019 Alleys](http://www.villageofshorewood.org/2019%20Alleys)
