




2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

Status Report # 9, June 7, 2019

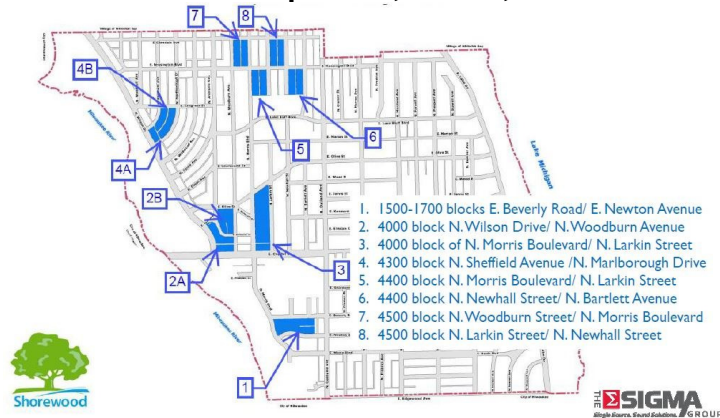

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

WORK COMPLETED FOR THE WEEK OF June 3, 2019

The final asphalt surface has been completed in all proposed asphalt alleyways (1, 2B, 3, 4B, 5, 6, 7, and 8) by Stark Pavement. Vehicle access to the alleys and adjoining garages has been restored for normal use.

Breckenridge Landscape completed installation of brick pavers in alleys 2A and 4A. (Green Alleys) Access to both alleys has been restored except for the entrance on the east end of 2A – which requires additional asphalt work near the curb line.

WORK SCHEDULED FOR THE WEEK OF June 10, 2019

Remaining work under the alley project will be schedule throughout the week;

- Stark Pavement will complete the installation of the necessary asphalt at the east entrance to alley 2A. (parking lot and curb line)
- T.P. Concrete will complete various concrete replacement areas throughout the project.
- All-Ways Contractors will begin soft restoration of the project including grading, placing topsoil, seed, and mulch throughout the project.

Alley access has been restored in all alleys.

Should you have any questions, please feel free to contact one of the following:

Chris Ball, Onsite Representative - 262-388-0705

Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019 Alleys](http://www.villageofshorewood.org/2019%20Alleys)
