




2019 ALLEY RECONSTRUCTION PROJECT CONSTRUCTION STATUS REPORT

Status Report # 7, May 24, 2019

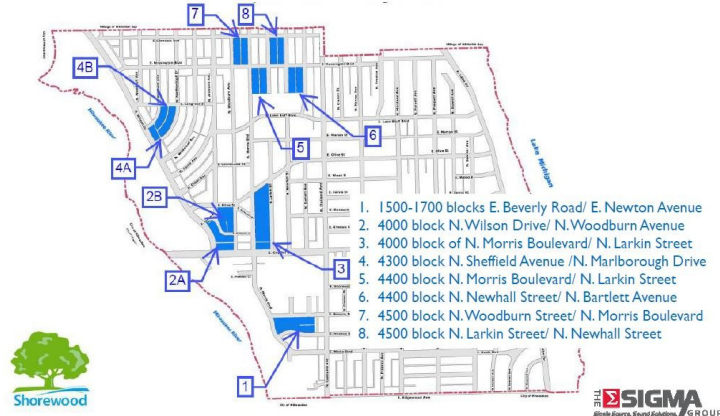

This Status Report will provide an update on the 2019 Alley Reconstruction Project's recent and upcoming work.

WORK COMPLETED FROM May 20, 2019 THROUGH May 24, 2019

T.P. Concrete completed concrete pouring in alleys 2A and 4A. After completion, All Ways construction prepped the remaining in areas for installation of brick pavers. Concrete pours were also completed on the alleyway entrances at 2A, 4B, and 8. Concrete driveway approach repairs were also completed in all alleys.

Access to garages in alleys 4A and 2A will continue to be restricted until brick pavers are installed.

WORK SCHEDULED FOR THE WEEK OF May 27, 2019

Breckenridge Construction will begin installing brick pavers in alley 2A and 4A after Memorial Day. Alley and garage access remain unavailable until brick pavers are installed.

Stark Pavement is scheduled to begin paving the surface layer of asphalt in alleys 1, 2B, 3, 4B, 5, 6, 7, and 8. Notifications regarding access restrictions during the asphalt paving will be distributed prior to alley closures.

If you have any questions, please feel free to contact one of the following:

Chris Ball, Onsite Representative - 262-388-0705

Shorewood DPW 414-847-2650

[www.villageofshorewood.org/2019 Alleys](http://www.villageofshorewood.org/2019%20Alleys)
